



MEASURE M CONSTRUCTION PROJECTS AND DEMOGRAPHICS REPORT April 2017

Chancellor: Bruce Baron

Vice Chancellor: Jose Torres

Program Manager: Kitchell/BRj

Report Date: 5/24/2017

SAN BERNARDINO VALLEY COLLEGE

Project: New Gymnasium (and Stadium)
Program: SBCCD Measure M Bond Program - Valley College

Report Date: April 30, 2017
Samir Shah, Sr. Project Manager

Progress This Period

- The light guage framing is finishing at Bldg. C and starting at D.
- Buildings B1 and B2 dried in; all rough-in ongoing.
- MEPs going into Bldg. D
- Change Order #18 in the works; awaiting response on a few PCIs from Swinerton for clarification.
- Commissioning final sign-off awaiting clarification on 5 items from HMC. Swinerton has completed all log items for CX to visit site and sign-off.
- LEED: Pending Swinerton submitting items in the logs prepared by HMC.
- The bleacher footings are dug, rebar was tagged and sampled at factory, and installation is ongoing. The masons completed blocks and grout is scheduled. Standing seam roofing at B1 & B2 ongoing.
- Decorative fence on the north side is ongoing and mow strip poured; the scoreboard is completed.
- Power shut down scheduled to energize Phase 4. Landscape work ongoing and some areas will be delivered to the District soon.

Items to Resolve

- \$452,508 remaining change order to remove wet/clay soil from the site and import base material. Several review meetings held with District and Counsel to reach an agreement. Decision pending.
- TIAs for Jan, Feb, and March schedules in discussion with District. Kitchell completed a response and, upon District approval, will send and request a scheduling meeting to finalize this issue. PCI: \$625,000
- Several Swinerton PCIs have been rejected for no merit. Swinerton expressed intent to dispute/claim them with the District- \$ 91,760.

Work Planned Next Period

- Continue Commissioning items for the final report for Gym Building.
- LEED coordination call between Swinerton and HMC scheduled.
- Dry-in for all remaining buildings.
- Get information for Dance Floor from District and complete PO process to place the order.
- Continue with site work in Phase IV.
- Track and finalize delivery of FF&E and other Campus-request items.

Notes

- Contractual completion date for the project is 2/13/17.
- **GC's March 2017 schedule update shows completion on 7/17/17**, which is 154 days behind schedule. April 2017 schedule is pending submission from General Contractor at the time of this reporting.
- Total of 9 rain days remaining of the total 44 days in the schedule.

Project: Applied Technology (Phase I)
Program: SBCCD Measure M Bond Program - Valley College


Report Date: April 30, 2017
 Kesi Sekhon, Project Manager

Project Budget	Planned		Spent to Date		Projected at Completion		Projected (Over) / Under Budget	
Project Hard Costs	2,726,675.00	68.38%	2,101,354.00	77.07%	2,105,253.85	77.21%	*	621,421.15 22.79%
Project Soft Costs	1,260,997.00	31.62%	663,642.14	52.63%	658,855.89	52.25%		602,141.11 47.75%
Total Project	3,987,672.00	100.00%	2,764,996.14	69.34%	2,764,109.74	69.32%		1,223,562.26 30.68%

*Note: Moved \$225,000 to AT from ADA scope for ADA requirements in the AT Building

Change Orders to Date * No. 2 * C.O. Totals 13,061.00 0 Change Amend. 0.00 0.62% of Hard Costs *

Project Schedule

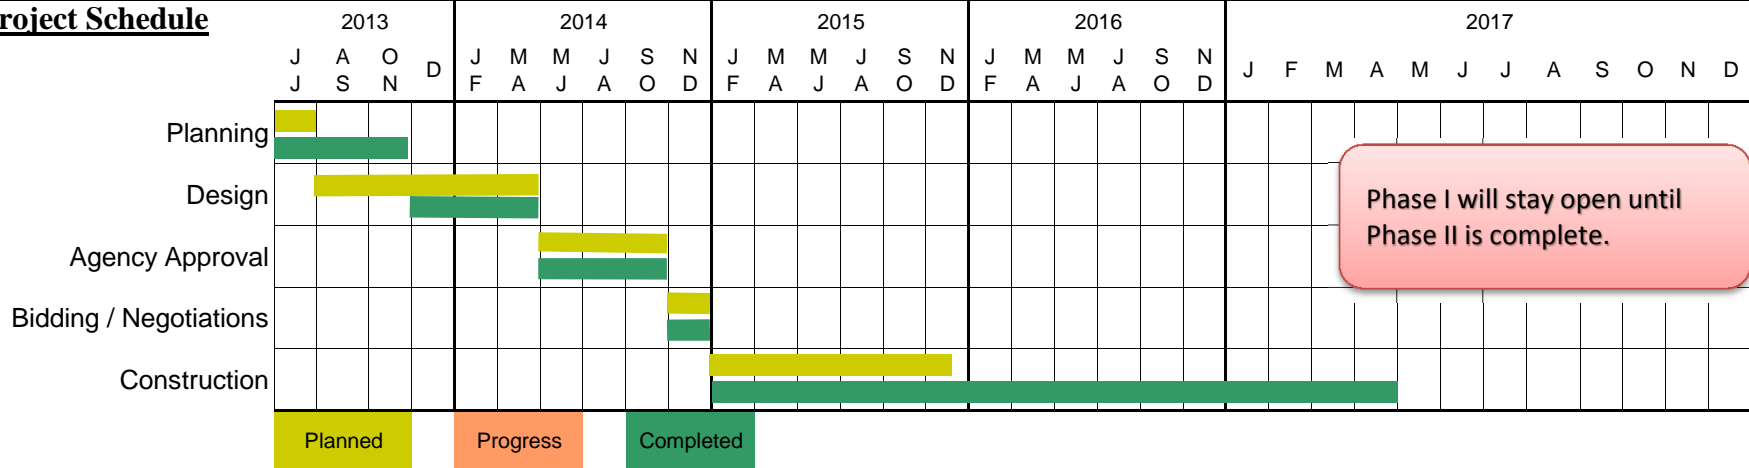

Progress Photos



Auto Body Lab 119



Welding Booths Lab 121



Auto Body Classroom 118

Project: Applied Technology (Phase I)
Program: SBCCD Measure M Bond Program - Valley College

Report Date: April 30, 2017
Kesi Sekhon, Project Manager

<p><u>Progress This Period</u></p> <ul style="list-style-type: none">• None	<p><u>Items to Resolve</u></p> <ul style="list-style-type: none">• None
<p><u>Work Planned Next Period</u></p> <ul style="list-style-type: none">• None	<p><u>Notes</u></p> <ul style="list-style-type: none">• DSA certification of Phase I and DSA certification of Phase II are complete.• This is the final monthly report.


Project: Applied Technology II (Phase II)
Program: SBCCD Measure M Bond Program - Valley College

Report Date: April 30, 2017
 Kesi Sekhon, Project Manager

Project Budget	Planned		Spent to Date		Projected at Completion		Projected (Over) / Under Budget	
Project Hard Costs	550,000.00	59.14%	241,256.85	43.86%	242,079.00	44.01%	*	307,921.00 55.99%
Project Soft Costs	380,000.00	40.86%	144,826.50	0.00%	236,347.50	62.20%		143,652.50 37.80%
Total Project	930,000.00	100.00%	386,083.35	41.51%	478,426.50	51.44%		451,573.50 48.56%

*Note: Moved \$225,000 to AT from ADA scope for ADA requirements in the AT Building

Change Orders to Date	* No. 0	* Change Order	0.00	0	Change Amend.	0.00	0.00%	of Hard Costs	*
-----------------------	---------	----------------	------	---	---------------	------	-------	---------------	---

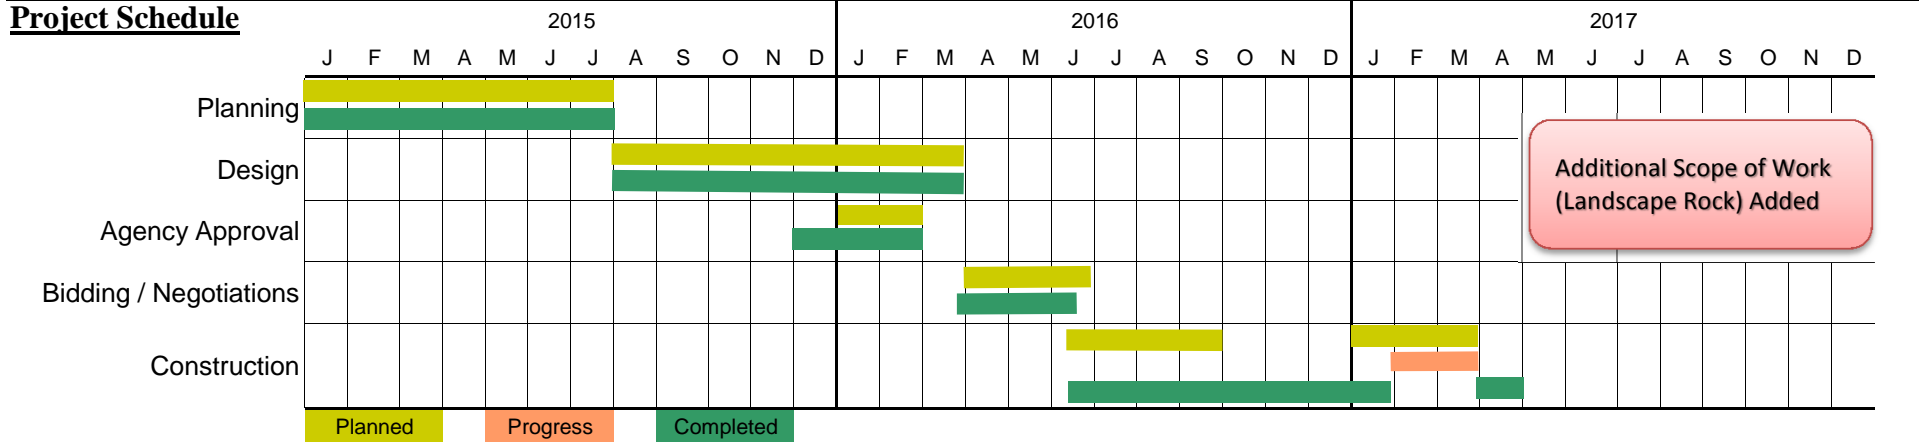

Progress Photos



Completed Men's Partition



Men's Lavatory and Mirror



Typical Transition and Diffuser (Aero Lab)

Project: Applied Technology II (Phase II)
Program: SBCCD Measure M Bond Program - Valley College

Report Date: April 30, 2017
Kesi Sekhon, Project Manager

<p><u>Progress This Period</u></p> <ul style="list-style-type: none">• None	<p><u>Items to Resolve</u></p> <ul style="list-style-type: none">• None
<p><u>Work Planned Next Period</u></p> <ul style="list-style-type: none">• None	<p><u>Notes</u></p> <ul style="list-style-type: none">• DSA certification of Phase I and DSA certification of Phase II are complete.• This is the final monthly report.

Activity Name	Rem Dur	Start	Finish	2013				2014				2015				2016				2017				8
				Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	
SBVC - Applied Technology Renovation - Phase II	61	01-Aug-15 A	30-Dec-16																					
Design	0	01-Aug-15 A	04-Mar-16 A																					
Bid & Award	0	04-Mar-16 A	09-Jun-16 A																					
Construction	0	13-Jun-16 A	28-Oct-16 A																					
Closeout	61	31-Oct-16*	30-Dec-16																					
SBVC - Gym Demolition, Home Bleachers, Site Work	778	15-Dec-11 A	16-May-17																					
Design	0	15-Dec-11 A	22-Jun-12 A																					
DSA Review	0	25-Jun-12 A	29-Apr-14 A																					
DSA Review (On Hold per District)	0	25-Jun-12 A	19-Mar-13 A																					
Bid & Award	0	12-Mar-14 A	13-Jun-14 A																					
Construction	736	13-Jun-14 A	04-Apr-17																					
Closeout	92	14-Feb-17	16-May-17																					
SBVC - Applied Technology Building - Phase I	0	03-Jun-13 A	29-Jan-16 A																					
Design	0	03-Jun-13 A	16-Mar-14 A																					
DSA Review	0	17-Mar-14 A	30-Sep-14 A																					
Bid & Award	0	01-Oct-14 A	18-Jan-15 A																					
Construction	0	19-Jan-15 A	31-Oct-15 A																					
Closeout	0	31-Oct-15 A	29-Jan-16 A																					

Layout: - SBCCD - SBVC Master Schedule - Summary
 Filters: TASK filter: - Summ Project Status.
 Page: 1 of 1

	Summary		Bid
	Summary		FF&E / AV and IT
	Assessment		FF&E and IT
	Programming Phase		Construction
	Design		Closeout
	DSA		Campus Moves

**San Bernardino Community College District
 Program Schedule
 Updated through April 30, 2017**


Kitchell / BRJ
 Program & Construction Managers

CRAFTON HILLS COLLEGE

Project: Occupational Education #2 (OE2)
Program: SBCCD Measure M Bond Program - Crafton Hills College

Report Date: April 30, 2017
 Brooke Duncan, Project Manager

Project Budget	Planned		Spent to Date		Projected at Completion		Projected (Over) / Under Budget	
Project Hard Costs	18,071,142.62	77.49%	17,827,122.92	98.65%	19,315,902.87	106.89%	(1,244,760.25)	-6.89%
Project Soft Costs	5,249,663.38	22.51%	5,723,305.95	109.02%	5,766,954.12	109.85%	(517,290.74)	-9.85%
Total Project	23,320,806.00	100.00%	23,550,428.87	100.98%	25,082,856.99	107.56%	(1,762,050.99)	-7.56%
Change Orders to Date * No. 8 * Change Order		992,473.72 * Change Amend.		38,321.93		5.14% of Hard Costs *		

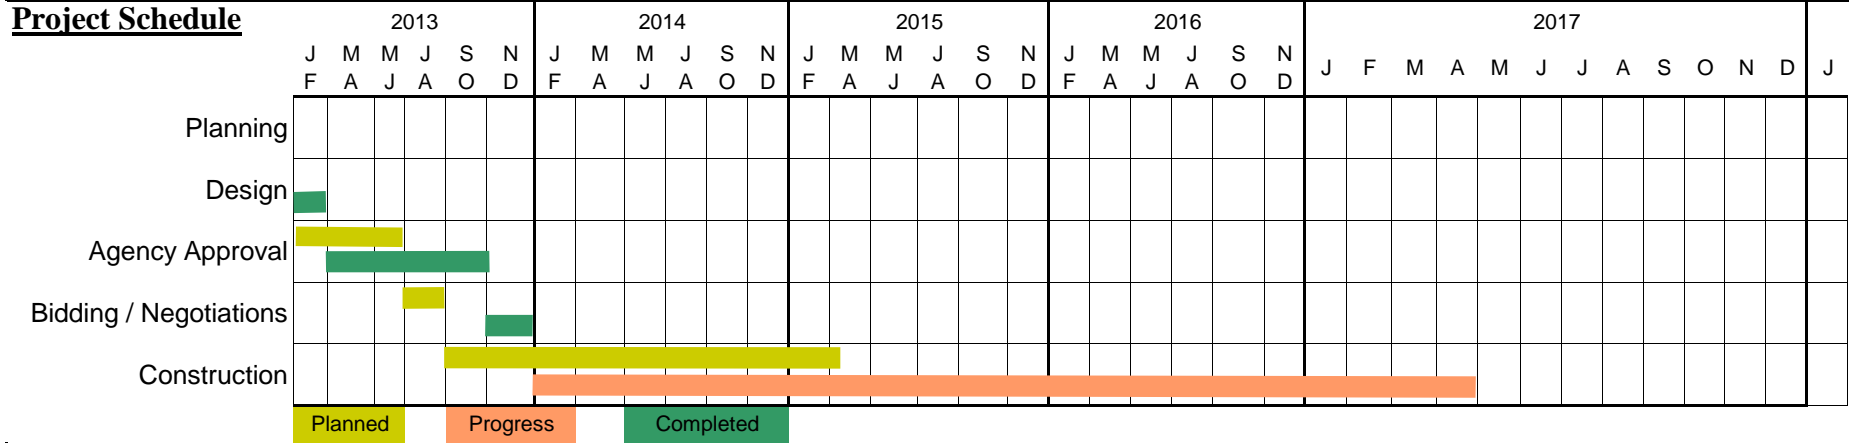

Project: Occupational Education #2 (OE2)
Program: SBCCD Measure M Bond Program - Crafton Hills College

Report Date: April 30, 2017
Brooke Duncan, Project Manager

<p><u>Progress This Period</u></p> <p>Building Package</p> <ul style="list-style-type: none">• District approved settlement agreement with Contractor.• Project has been submitted for LEED review.• Final DSA forms submitted for certification. <p>Fire Hose Pump</p> <ul style="list-style-type: none">• Complete, project closed.	<p><u>Items to Resolve</u></p> <ul style="list-style-type: none">• Kitchell/BRj has preformed a schedule analysis and provided its findings/recommendations to the District for review. <p>Fire Hose Pump</p> <ul style="list-style-type: none">• None
<p><u>Work Planned Next Period</u></p> <p>Building Package</p> <ul style="list-style-type: none">• Achieve DSA Certification.• Resolve Stop Payment Notices and DIR Claim.• File Notice of Completion.	<p><u>Notes</u></p> <ul style="list-style-type: none">• None

Project: **PE Complex**

Report Date: April 30, 2017

Program: SBCCD Measure M Bond Program - Crafton Hills College

Brooke Duncan, Project Manager

Project Budget	Planned		Spent to Date		Projected at Completion		Projected (Over) / Under Budget	
Project Hard Costs	5,087,499.57	73.18%	4,867,164.20	95.67%	4,993,441.83	98.15%	94,057.74	1.85%
Project Soft Costs	1,864,581.04	26.82%	2,096,454.01	112.44%	2,120,680.76	113.73%	(256,099.72)	-13.73%
Total Project	6,952,080.61	100.00%	6,963,618.21	100.17%	7,114,122.59	102.33%	(162,041.98)	-2.33%
Change Orders to Date	* No.	4	* Change Order	99,009.46	* Change Amend.	0.00	0.00% of Hard Costs 1.95%	

Project Schedule	2013				2014					2015					2016					2017														
	J	M	J	N	J	M	M	J	S	N	J	M	M	J	S	N	J	M	M	J	S	N	J F M A M J J A S O N D J											
	F	A	J	O	F	A	J	A	O	D	F	A	J	A	O	D	F	A	J	A	O	D	J	F	M	A	M	J	J	A	S	O	N	D
Planning																																		
Design																																		
Agency Approval	█																																	
Bidding / Negotiations		█	█																															
Construction																																		
	Planned				Progress					Completed																								

Completion Photos



Front of Building



Path of Travel to the KHA/PE Complex

Project: PE Complex

Report Date: April 30, 2017

Program: SBCCD Measure M Bond Program - Crafton Hills College

Brooke Duncan, Project Manager

<p><u>Progress This Period</u></p> <ul style="list-style-type: none">• Architect is reviewing LEED points for resubmission.• LEED upload to USGBC: Response: 11 points are pending further clarification.	<p><u>Items to Resolve</u></p> <ul style="list-style-type: none">• Notice of Completion will not be filed until claim is released or settled with DIR (Department of Industrial Relations).• DIR update: This matter is still active and pending.• All other Contractor deliverables are complete and closed-out.
<p><u>Work Planned Next Period</u></p> <ul style="list-style-type: none">• OCIP water intrusion claim for Yoga Studio flooring to be submitted.	<p><u>Notes</u></p> <ul style="list-style-type: none">• N/A

Project: Laboratory/Administration Renovation (LADM)
Program: SBCCD Measure M Bond Program - Crafton Hills College

Report Date: April 30, 2017
 Leilani Nunez, Project Manager

Project Budget	Planned		Spent to Date		Projected at Completion		Projected (Over) / Under Budget	
Project Hard Costs	12,057,810.18	77.78%	9,158,339.14	75.95%	11,655,963.52	96.67% *	401,846.66	3.33%
Project Soft Costs	3,443,800.82	22.22%	3,196,675.01	92.82%	3,886,136.28	112.84% *	(442,335.46)	-12.84%
Total Project	15,501,611.00	100.00%	12,355,014.15	79.70%	15,542,099.80	100.26%	(40,488.80)	-0.26%

Change Orders to Date * No. 4 * Change Order 367,530.24 * Change Amend. 0.00 3.05% of Hard Costs *

Project Schedule	2012	2013				2014				2015				2016				2017																																			
	S O	J	M	M	J	S	N	J	M	M	J	S	N	J	M	M	J	S	N																																		
	D	F	A	J	A	O	D	F	A	J	A	O	D	F	A	J	A	O	D	F	A	M	J	J	A	S	O	N	D																								
Planning	█				█																																																
Design		█	█	█	█	█	█																																														
Agency Approval																																																					
Bidding / Negotiations																																																					
Construction																																																					
		Planned	Progress				Completed				On Hold																																										

Progress Photos



04/24/2017

Flooring at 3rd Floor Classroom



04/26/2017

Landscape Remediation



04/18/2017

AV/IT Equipment

Project: LADM (Laboratory/Administration Renovation)
Program: SBCCD Measure M Bond Program - Crafton Hills College

Report Date: April 30, 2017
Leilani Nunez, Project Manager

<p><u>Progress This Period</u></p> <ul style="list-style-type: none">• Electrical finish ongoing.• Exterior handrails ongoing.• Mechanical controls ongoing.• Floor prep for carpet and linoleum on 1st floor ongoing.• Carpet and linoleum on 3rd and 2nd floors complete.• Elevator installation ongoing.• Fire alarm programming started.• AV/IT equipment installation ongoing.• Roof punch completed.• Landscape remediation ongoing.• Hardware ongoing.	<p><u>Items to Resolve</u></p> <ul style="list-style-type: none">• Project is 53 days behind schedule. KB is in negotiations with the General Contractor to address and resolve schedule delays and costs.
<p><u>Work Planned Next Period</u></p> <ul style="list-style-type: none">• Complete electrical.• Complete mechanical controls.• Begin air balancing of HVAC and commissioning.• Complete flooring.• Complete elevator.• Complete final paint at all levels.• Complete fire alarm programming and testing.• Complete exterior handrails.• Complete hardware at all levels.• Complete signage.• Start interior punch.	<p><u>Notes</u></p> <ul style="list-style-type: none">• This project includes the Design/Build replacement of the Fire Alarm Panel at Central Complex 2.

Project: CHS Fire Alarm Replacement PHL
 (located within LADM Bldg.)

Report Date: April 30, 2017


Program: SBCCD Measure M Bond Program - Crafton Hills College

Brooke Duncan, Project Manager

Project Budget	Planned		Spent to Date		Projected at Completion		Projected (Over) / Under Budget	
Project Hard Costs	30,884.65	75.54%	0.00	0.00%	30,884.65	100.00%	0.00	0.00%
Project Soft Costs	10,000.00	24.46%	0.00	N/A	10,000.00	N/A	0.00	N/A
Total Project	40,884.65	100.00%	0.00	0.00%	40,884.65	100.00%	0.00	0.00%

Note: This contract amount is included in the LADM total budget.


Change Orders to Date	* No.	* Change Order	* Change Amend.	0.00	N/A of Hard Costs	*
-----------------------	-------	----------------	-----------------	------	-------------------	---

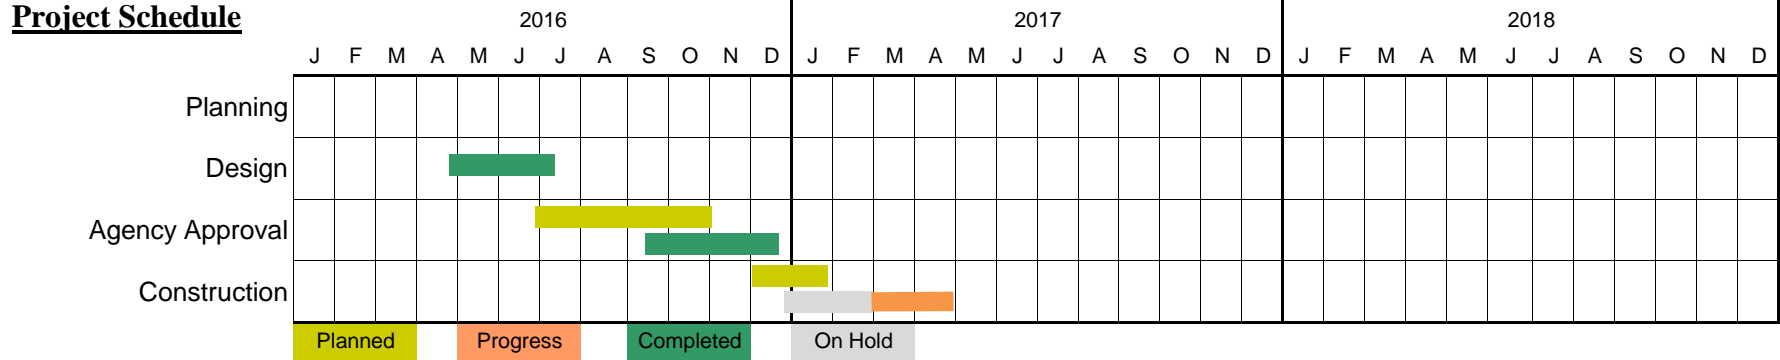

Progress Photos



Existing Fire Alarm Panel

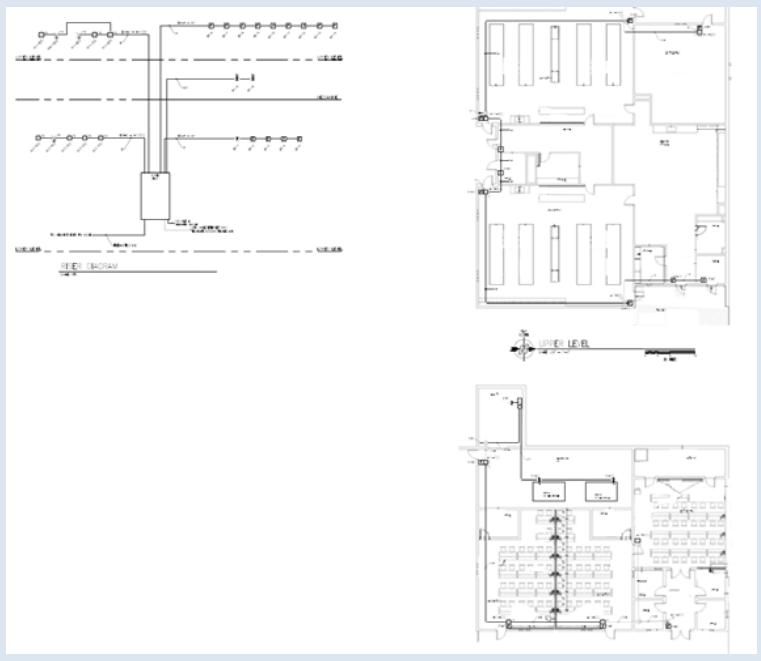

Design Drawings

Project: CHS Fire Alarm Replacement PHL

(located within LADM Bldg.)

Report Date: April 30, 2017

Program: SBCCD Measure M Bond Program - Crafton Hills College

Brooke Duncan, Project Manager

Progress This Period

- Scope of work complete. Contractor to submit DSA forms.

Items to Resolve

- None

Work Planned Next Period

- DSA Certification.

Notes

- None

Project: Student Services A Renovations (SSA)

Report Date: April 30, 2017

Program: SBCCD Measure M Bond Program - Crafton Hills College




Brooke Duncan, Project Manager

Project Budget	Planned		Spent to Date		Projected at Completion		Projected (Over) / Under Budget	
Project Hard Costs	5,549,055.30	73.38%	3,962,341.48	71.41%	6,059,944.74	109.21% *	(510,889.44)	-9.21%
Project Soft Costs	2,013,411.70	26.62%	2,311,165.68	114.79%	2,721,814.73	135.18% *	(708,403.03)	-35.18%
Total Project	7,562,467.00	100.00%	6,273,507.16	82.96%	8,781,759.47	116.12%	(1,219,292.47)	-16.12%

Change Orders to Date * No. 2 * Change Order 91,983.23 * Change Amend. 0.00 1.52% of Hard Costs *

Project Schedule	2014					2015					2016												2017														
	J	M	M	J	S	N	J	M	M	J	S	N	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J
	F	A	J	A	O	D	F	A	J	A	O	D																									
Planning																																					
Design																																					
Agency Approval																																					
Bidding / Negotiations																																					
Construction																																					

Progress Photos

 <p>04/28/2017</p> <p>Mechanical Room 2nd Floor</p>	 <p>04/28/2017</p> <p>Room Signage</p>	 <p>04/28/2017</p> <p>New Carpeting</p>
---	---	---

Project: Student Services A (SSA Renovations)
Program: SBCCD Measure M Bond Program - Crafton Hills College

Report Date: April 30, 2017
Brooke Duncan, Project Manager

<p><u>Progress This Period</u></p> <ul style="list-style-type: none">• AHUs installed.• Complete all concrete scope of work.• Set all light and plumbing fixtures.• Close ceilings.• Interior paint.• Install doors and hardware.• Complete restroom tile.• Certification of elevator.	<p><u>Items to Resolve</u></p> <ul style="list-style-type: none">• The Project is 50 days behind schedule.• Schedule extension was provided for delay days. Substantial Completion is targeted for 5/25/17.
<p><u>Work Planned Next Period</u></p> <ul style="list-style-type: none">• Punch List.• Complete all costs for the project.• Fire Alarm testing.• Install furniture and equipment.• Substantial Completion 5/25/17.	<p><u>Notes</u></p> <ul style="list-style-type: none">• Per District request, award of contract for March 2016 bid opening postponed to May 2016 Board.• Per District direction in April 2016, project was rebid.

Project: Student College Center (SCC)
Program: SBCCD Measure M Bond Program - Crafton Hills College

Report Date: April 30, 2017
 Brooke Duncan, Project Manager

Project Budget	Planned		Spent to Date		Projected at Completion		Projected (Over) / Under Budget			
Project Hard Costs	3,174,000.00	80.17%	0.00	0.00%	*	0.00	0.00%	*	3,174,000.00	100.00%
Project Soft Costs	784,864.00	19.83%	416,872.67	53.11%		416,872.67	53.11%		367,991.33	46.89%
Total Project	3,958,864.00	100.00%	416,872.67	10.53%		416,872.67	10.53%		3,541,991.33	89.47%

*** NOTE: INCLUDES FIRE ALARM SYSTEM UPGRADES**
 Change Orders to Date * No. 0 * Change Order 0.00 * Change Amend. 0.00 0.00% of Hard Costs *

Project Schedule	2012			2013			2014				2015				2016				2017																	
	JF	MJ	SO	JF	MJ	SO	J	M	M	J	S	N	J	M	M	J	S	N	J	M	M	J	S	N	J	F	M	A	M	J	J	A	S	O	N	D
	MA	JA	ND	MA	JA	ND	F	A	J	A	O	D	F	A	J	A	O	D	F	A	J	A	O	D	J	F	M	A	M	J	J	A	S	O	N	D
Planning																																				
Design																																				
Agency Approval																																				
Bidding / Negotiations																																				
Construction																																				
	Planned			Progress			Completed				On Hold																									


Progress Photos



Exterior Building Photo of East Elevation



1st Floor

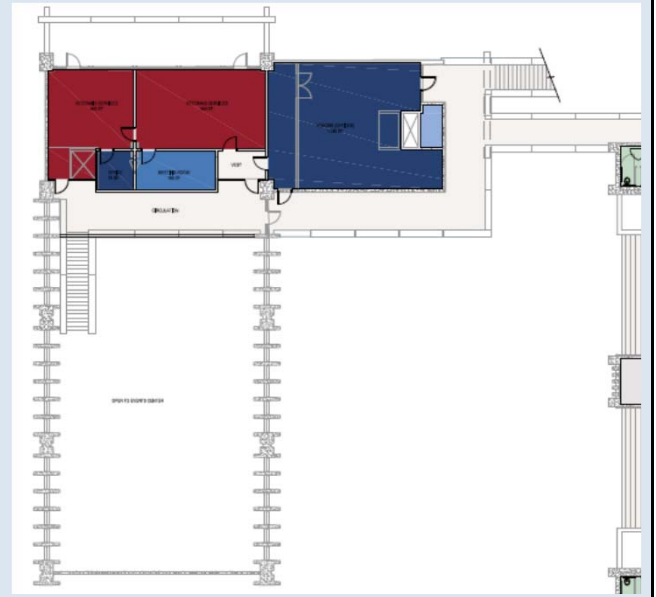

2nd Floor

Project: Student College Center (SCC)
Program: SBCCD Measure M Bond Program - Crafton Hills College

Report Date: April 30, 2017
Brooke Duncan, Project Manager

<p><u>Progress This Period</u></p> <ul style="list-style-type: none">• On hold until notified by the District.	<p><u>Items to Resolve</u></p> <ul style="list-style-type: none">• None
<p><u>Work Planned Next Period</u></p> <ul style="list-style-type: none">• N/A	<p><u>Notes</u></p> <ul style="list-style-type: none">• None

Project: PAC: Marquee Sign

Report Date: April 30, 2017

Program: SBCCD Measure M Bond Program - Crafton Hills College

Brooke Duncan, Project Manager

Project Budget	Planned		Spent to Date		Projected at Completion		Projected (Over) / Under Budget	
Project Hard Costs	175,000.00	86.38%	0.00	0.00%	175,000.00	100.00%	0.00	0.00%
Project Soft Costs	27,585.28	13.62%	15,822.90	N/A	40,720.00	N/A	(13,134.72)	N/A
Total Project	202,585.28	100.00%	15,822.90	7.81%	215,720.00	106.48%	(13,134.72)	-6.48%
Change Orders to Date	* No.	* Change Order	* Change Amend.		0.00	N/A of Hard Costs		*

	2016												2017												2018											
	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
Planning																																				
Design																																				
Bidding / Negotiations																																				
Construction																																				

Planned Progress Completed On Hold

Design Photos

PAC Marquee Details

The image displays a set of architectural drawings for the PAC Marquee Sign. It includes an axonometric view of the sign structure, a plan view showing the layout of the sign, and several elevation and section views detailing the construction and materials. The drawings are accompanied by general notes and logos for DKC and Crafton Hills College. The title block identifies the project as 'PERFORMING ARTS CENTER MONUMENT SIGNAGE AND ART GALLERY SIGNAGE' and includes the drawing title 'MARQUEE PLAN, ELEVATIONS, AND SECTIONS' and sheet number 'A1.1'.

Project: PAC: Marquee Sign
Program: SBCCD Measure M Bond Program - Crafton Hills College

Report Date: April 30, 2017
Brooke Duncan, Project Manager

Progress This Period

- Project is on hold.

Items to Resolve

- None

Work Planned Next Period

- N/A


Notes

- N/A


Project: PAC: Battery / Sewer Controls
Program: SBCCD Measure M Bond Program - Crafton Hills College

Report Date: April 30, 2017
 Brooke Duncan, Project Manager

Project Budget	Planned		Spent to Date		Projected at Completion		Projected (Over) / Under Budget	
Project Hard Costs	160,000.00	79.97%	164,262.00	102.66%	164,262.00	102.66%	(4,262.00)	-2.66%
Project Soft Costs	40,070.00	20.03%	33,213.00	N/A	40,070.00	N/A	0.00	N/A
Total Project	200,070.00	100.00%	197,475.00	98.70%	204,332.00	102.13%	(4,262.00)	-2.13%
Change Orders to Date	* No.	* Change Order	* Change Amend.		0.00	N/A of Hard Costs		*

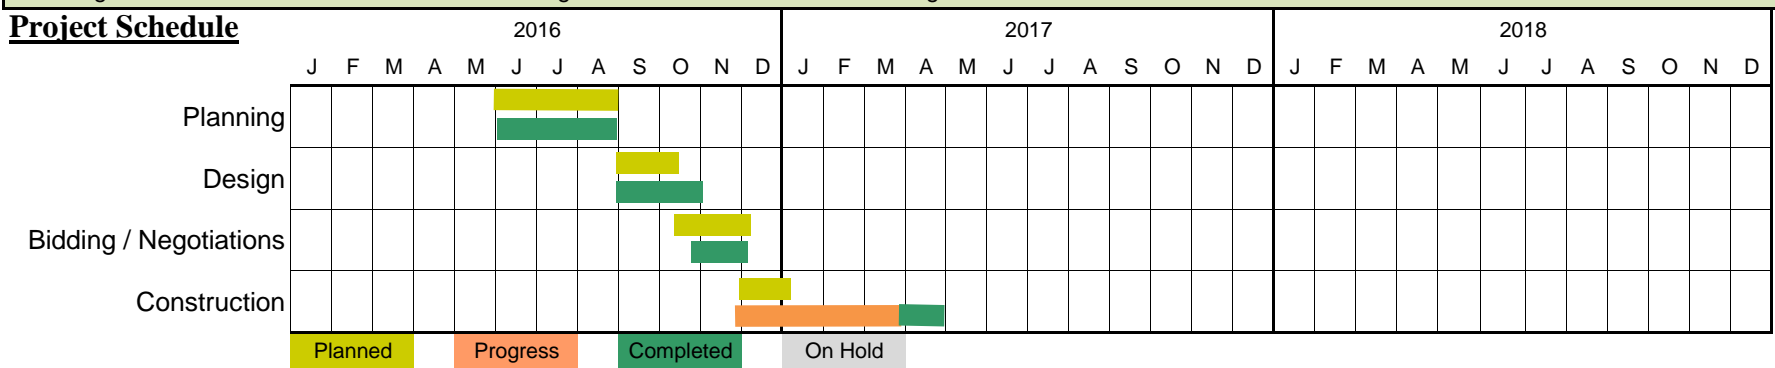

Progress Photos

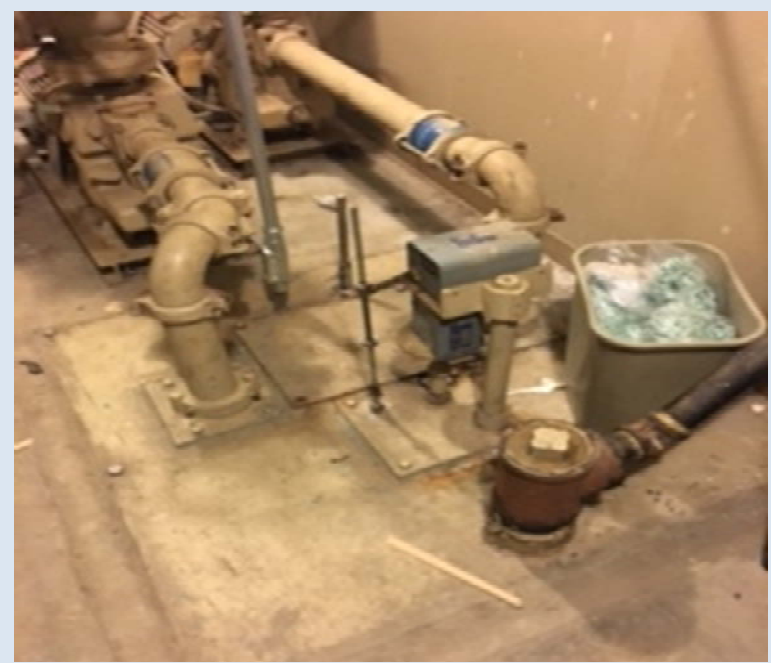


Project: PAC: Battery / Sewer Controls
Program: SBCCD Measure M Bond Program - Crafton Hills College

Report Date: April 30, 2017
Brooke Duncan, Project Manager

<p><u>Progress This Period</u></p> <ul style="list-style-type: none">• Project Complete. This is the final Monthly Report for this project.	<p><u>Items to Resolve</u></p> <ul style="list-style-type: none">• None
<p><u>Work Planned Next Period</u></p> <ul style="list-style-type: none">• None	<p><u>Notes</u></p> <ul style="list-style-type: none">• None

Project Budget	Planned		Spent to Date		Projected at Completion		Projected (Over) / Under Budget	
Project Hard Costs	0.00	0.00%	0.00	N/A	0.00	N/A	0.00	N/A
Project Soft Costs	85,000.00	100.00%	1,228.79	N/A	46,128.79	N/A	38,871.21	N/A
Total Project	85,000.00	100.00%	1,228.79	1.45%	46,128.79	54.27%	38,871.21	45.73%
Change Orders to Date * No.	* Change Order		* Change Amend.		0.00	N/A of Hard Costs		*

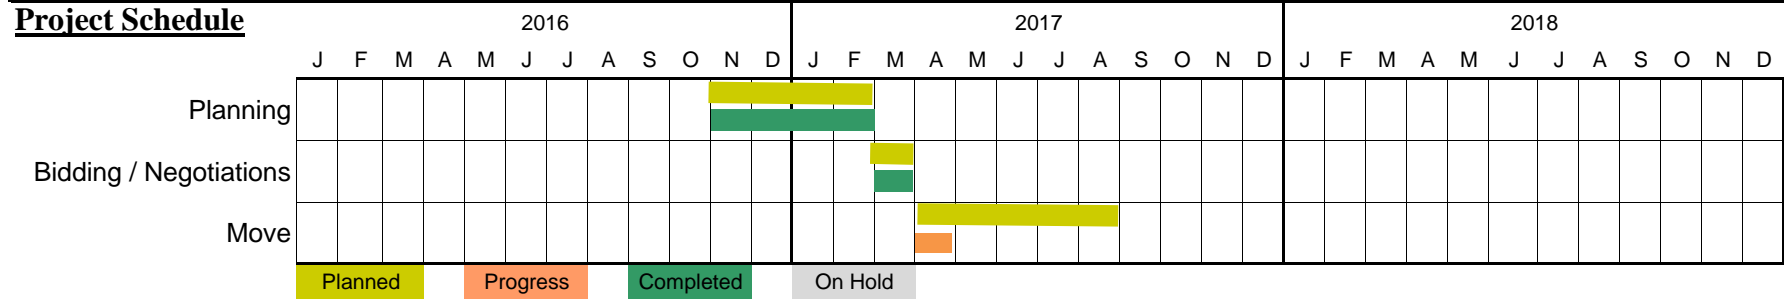

<p>Progress This Period</p> <ul style="list-style-type: none"> • Planning complete. • Contract awarded to Burgess Moving & Storage. • Moving labels and boxes distributed to participants of the move. 	<p>Items to Resolve</p> <ul style="list-style-type: none"> • None
--	---

<p>Work Planned Next Period</p> <ul style="list-style-type: none"> • No activities planned until June 2017 for Phase 1 move. 	<p>Notes</p> <ul style="list-style-type: none"> • None
--	--

Activity Name	Rem Dur	Start	Finish	2013 2014 2015 2016 2017 2018 2019																											
				2013				2014				2015				2016				2017				2018				2019			
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
SBCHC - Miscellaneous Bond Improvements: Campus CHUF	87	13-Sep-16 A	26-Jul-17																												
Programming Phase	2	13-Sep-16 A	02-May-17																												
Bid & Award	0	24-Jan-17 A	20-Apr-17 A																												
Campus Moves	47	09-Feb-17 A	18-Jul-17																												
Closeout	53	04-Jun-17	26-Jul-17																												
SBCHC - PAC Marquee Sign	87	04-Apr-16 A	25-Jul-17																												
Design	0	04-Apr-16 A	14-Oct-16 A																												
Bid & Award	20	12-Sep-16 A	29-May-17																												
Construction	28	30-May-17	26-Jun-17																												
Closeout	29	27-Jun-17	25-Jul-17																												
SBCHC - PAC Battery/Sewer Controls	0	06-Jun-16 A	27-Apr-17 A																												
Design	0	06-Jun-16 A	05-Sep-16 A																												
Bid & Award	0	05-Sep-16 A	03-Nov-16 A																												
Construction	0	04-Nov-16 A	31-Mar-17 A																												
Closeout	0	31-Mar-17 A	27-Apr-17 A																												
SBCHC - New Occupational Education 2 - OE2 Building / Site	0	21-Oct-13 A	30-Apr-17																												
Bid & Award	0	21-Oct-13 A	13-Dec-13 A																												
Construction	0	16-Dec-13 A	01-Dec-15 A																												
Closeout	0	20-Oct-15 A	30-Apr-17																												
FF&E and IT	0	13-Apr-15 A	31-Dec-15 A																												
Campus Moves (Into Building)	0	16-Oct-15 A	03-Dec-15 A																												
SBCHC - PE / ADA Access to Aquatic Center / Gym Demo	246	12-Jan-12 A	31-Dec-17																												
Design	0	12-Jan-12 A	12-Oct-12 A																												
DSA Review	0	13-Oct-12 A	08-May-13 A																												
Bid & Award	0	09-May-13 A	09-Aug-13 A																												
Construction	0	10-Aug-13 A	31-Jul-14 A																												
Closeout	246	01-Aug-14 A	31-Dec-17																												
SBCHC - Student Services A Seismic Upgrade and Renovation	66	08-Aug-12 A	05-Jul-17																												
Programming Phase	0	08-Aug-12 A	08-May-13 A																												
Design	0	09-May-13 A	16-Dec-13 A																												
DSA Review	0	17-Dec-13 A	30-Oct-14 A																												
Bid & Award	0	09-Dec-15 A	18-Jul-16 A																												

Layout: - SBCCD - SBCHC Master Schedule - Summary
 Filters: TASK filter: - Summary Project Status.













	Summary		Construction
	Summary		Closeout
	Assessment		FF&E and IT
	Programming Phase		FF&E / AV and IT
	Design		Campus Moves
	DSA		
	Bid		

San Bernardino Community College District
 Program Schedule
 Updated through April 30, 2017

Kitchell / BRJ
 Program & Construction Managers

Activity Name	Rem Dur	Start	Finish	2013 2014 2015 2016 2017 2018 2019																											
				2013				2014				2015				2016				2017				2018				2019			
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Construction	19	18-Jul-16 A	25-May-17																												
Closeout	41	08-May-17	05-Jul-17																												
Punch List work	21	08-May-17	06-Jun-17																												
Campus Moves	5	03-Jun-17	09-Jun-17																												
SBCHC - LADM Seismic Upgrades and Renovations	93	02-Jan-13 A	31-Jul-17	▶																											
Design	0	02-Jan-13 A	16-Dec-13 A																												
DSA Review	0	17-Dec-13 A	30-Oct-14 A																												
Bid & Award	0	09-Dec-15 A	15-Apr-16 A																												
Construction	33	15-Apr-16 A	01-Jun-17																												
Closeout	60	02-Jun-17	31-Jul-17																												
Campus Moves	5	17-Jul-17	21-Jul-17																												
SBCHC - Student Center / Cafeteria (College Center) Seismic	694	30-Oct-14 A	24-Mar-19	▶																											
Design	180	30-Oct-14 A	26-Oct-17																												
DSA Review	167	27-Oct-17	11-Apr-18																												
Bid and Award	77	12-Apr-18	27-Jun-18																												
Construction	210	28-Jun-18	23-Jan-19																												
Closeout	60	24-Jan-19	24-Mar-19																												

Layout: - SBCCD - SBCHC Master Schedule - Summary
 Filters: TASK filter: - Summary Project Status.

- | | | | |
|---|-------------------|---|------------------|
|  | Summary |  | Construction |
|  | Summary |  | Closeout |
|  | Assessment |  | FF&E and IT |
|  | Programming Phase |  | FF&E / AV and IT |
|  | Design |  | Campus Moves |
|  | DSA | | |
|  | Bid | | |

San Bernardino Community College District
 Program Schedule
 Updated through April 30, 2017

Kitchell / BRJ
 Program & Construction Managers
