

SAN BERNARDINO COMMUNITY COLLEGE DISTRICT
CRAFTON HILLS COLLEGE CAMPUS



NEWSLETTER

2024
QUARTER 3



Performing Arts Center

Design Team: DLR Group
Contractor: Bernards Bros.
Scheduled Completion: Fall 2025
Construction Completion: 28%

Description: 23,944 GSF two building complex to replace the existing Performing Arts Building.

Status Update: Bldg. A footings and shear wall work continues. Bldg. B footings and underground fire utility installation, ongoing. Sewer connection across Campus Drive completed over spring break.

Solar PV Upgrade

Design Team: Total Energies
Scheduled Completion: May 2024
Construction Completion: 92%

Description: Replacement of the campus's aging Solar PV tracker system with a new ground mounted fixed tile system complete with Tesla battery back up storage.

Status Update: PV panel installation 100% complete. Electrical feeders & PV equipment installed, pending final testing / commissioning & permission to operate from SCE.




Cooling Tower Replacement

Design Team: P2S
Contractor: Coutts
Construction Phase: Closeout

Description: Replacement of (2) aging cooling towers, system piping & valves update.

Status Update: Cooling towers & VFD's installed & are functioning, commissioning completed, site training completed.

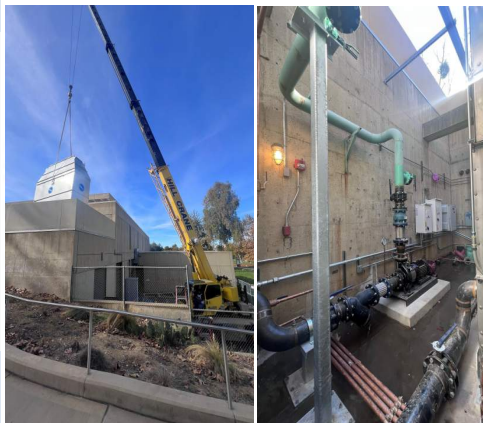

Projects In Construction

Campus Accessibility & Improvements
Phase 2
Central Complex 2 Renovation

Upcoming Projects

Instructional Building - Design
Crafton Hall Renovation - Awarded
Campus Infrastructure Projects

