

SAN BERNARDINO COMMUNITY COLLEGE DISTRICT CRAFTON HILLS COLLEGE CAMPUS



NEWSLETTER

4th Quarter
2024



Performing Arts Center

Design Team: DLR Group
Contractor: Bernards Bros.
Scheduled Completion: Fall 2025
Construction Completion: 38%

Description: 23,944 GSF two building complex to replace the existing Performing Arts Building.

Status Update: Structural welding ongoing at Buildings A and B, grading, stem wall form work ongoing, metal deck installations ongoing.

Solar PV Upgrade

Design Team: Total Energies
Scheduled Completion: August 2024
Construction Completion: 99%

Description: Replacement of the campus's aging Solar PV tracker system with a new ground mounted fixed tile system complete with Tesla battery back up storage.

Status Update: PV panels are in operation with permission to operate from SCE. Commissioning ongoing, coordination with SCE for metering ongoing.




Central Complex 2 Reno

Design Team: W.E. O'neil
Scheduled Completion: August 2024
Construction Completion: 82%

Description: Renovation of existing Building 11 to provide remodeled educational labs, updates to classroom finishes and lecture hall seating replacement.

Status Update: Building HVAC is in operation, electrical components have been installed, flooring and finishes installations are ongoing, exterior paver installations are proceeding.

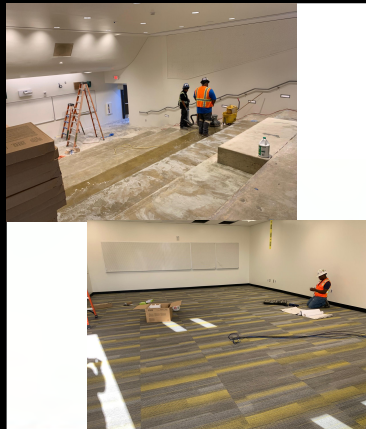

Projects In Construction

Crafton Hall Renovation: Project Kick Off July 2024.

Projects In Closeout:

Cooling Tower Replacement

Upcoming Projects

Instructional Building - Design
Campus Infrastructure Projects

